

Reporting by the project partners by work packages

UHC “Dr Dragisa Misovic – Dedinje”

**Management Board Meeting
Belgrade, 27-28 sep 2019.
Faculty of Medicine
No 8, Dr Subotica st.**

Project number: 585927-EPP-1-2017-1-RS-EPPKA2-CBHE-JP (2017 – 3109 / 001 – 001)

"This project has been funded with support from the European Commission. This publication reflects the views only of the author, and the Commission cannot be held responsible for any use which may be made of the information contained therein"

7	WORKPLAN for project year 1															
8																
9	Activities			Total duration (number of weeks)	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12
10	Ref.nr/ Sub-ref nr	Title														
11	1,1	Analysis of Pain medicine study program and LLL courses in PCs		3X												
12	1,2	Analysis of Pain medicine study program and LLL courses in PgCs		3=												
13	1,3	Comparative analysis of education offer of pain medicine in the PCs and PgCs			2X2=											
14	1,4	Analysis of labour market needs relevant for HCW in PCs			1X											
15	1,5	Purchasing of equipment				4X	4X	4X	4X	4X	4X	4X	4X	4X	4X	4X
16	2,1	Training of existing teaching staff from PCs at PgCs					3X3=	3X3=	1X1=	1X1=	1X1=	1X1=				
17	2,2	Development of HEPMP contents and Teaching material									4X	4X	4X	4X		
18	2,3.	Preparation and submission for accreditation of study program										2X				
19	5.1.	Preparing project dissemination strategy						2X1=								
20	5.2.	Creation of Web site of HEPMP			4X											
21	6.1.	Establishment of Quality control board		1X1=							1X1=					
22	6.2.	Development of control plan for quality assurance in teaching process			2X2=											
23	6,3.	Regular Quality board meetings			1X1=						1X1=					
24	7.1.	Establishment of management board		1X1=												
25	7.2.	Creation of project management guide			3X3=											
26	7.3.	Kick off meeting		2X1=												
27	7.4.	Regular management board meetings					1X2=				1X2=					
28	7.5.	Making a regular reports and final report		1X1=			1X1=				1X1=					
29																
30	WORKPLAN for project year 2															
31																
32	Activities			Total duration	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12
33	Ref.nr/ Sub-ref nr	Title														
34	1,5	Purchasing of equipment		4X	4X	4X										
35	2.4.	Enrollment of students at study program		1X												
36	2,5.	Implementation of study programs		4X	4X	4X	4X	4X	4X	4X	4X	4X	4X	4X	4X	4X
37	3.1.	Development of learning material for HCW in PCs		1X1=		1X1=		1X1=		1X1=		1X1=				
38	3.2.	National call and selection of trainees			1X		1X		1X		1X		1X		1X	
39	3.3.	Accreditation of LLL courses in PCs			1X		1X		1X		1X			1X		
40	3.4.	Delivering of LLL courses of pain medicine in primary health care centers of PCs						1X1=		1X1=		1X1=			1X1=	
41	4.1.	Establishment of regional academic network		1X1=												
42	4.2.	Establishment of PAINWB platform		4X	4X	4X	4X	4X	4X	4X	4X	4X	4X	4X	4X	4X
43	4.3.	Continuous selection of case studies for students and HCWs education							1X1=	1X1=	1X1=	1X1=	1X1=	1X1=	1X1=	1X1=
44	6.4.	Evaluation of student and participant satisfaction						1X		1X		1X			1X	
45	6,3.	Regular Quality board meetings						1X1=								1X1=
46	6,5	Monitoring visits by external evaluators														
47	7.4.	Regular management board meetings		1X2=				2X1=							2X1=	
48	7.5.	Making a regular reports and final report		1X1=				1X1=							1X1=	
49																
	WORKPLAN for project year 3															

WORKPLAN for project year 3														
Activities		Total dura	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12
Ref.nr/ Sub-r	Title													
2,5	Implementation of study programs		4X	4X	4X	4X	4X	4X	4X	4X	4X	4X	4X	4X
3,5	Delivering of interventional pain trainings in PCs		1X1=											
4,3	Continous selection of case studies for students and HCWs education		1X1=	1X1=	1X1=	1X1=	1X1=	1X1=	1X1=	1X1=	1X1=	1X1=	1X1=	1X1=
4,4	Analysis of systematic standards and procedures in the area of PM												3X3=	
5,3	Promotion of HEPMP program Events			1X		1X1=								1X1=
5,4	Developing institutional websites, newsletter, promotional material and media			1X			1X			1X			1X	
5,5	Dissemination of instituional websites, newsletter, promotional material and me					1X			1X					
5,6	Signing cooperation between HEIs and relevant stakeholders										1X			
6,4	Evaluation of student and participant satissfaction		1X1=											
6,5	Regular Quality board meetings		1X1=											1X1=
7,4	Regular management board meetings		2X1=					2X1=						2X1=
7,5	Making a regular reports and final report		1X1=					1X1=						1X1=

- **WP1 (Comparative analysis of education offer in Pain Medicine)**
 - 1.4. Analysis of labour market needs relevant for HCW in PCs**
Labour Market Needs Serbia – Situation analysis
Dr sci. Zoran Vlahović i Prof. dr Perunović – may 2018, Rijeka
- **WP2 (Development of joint curricula for PM study program)**
 - 2.1. Training of existing teaching staff from PCs at PgCs**
1st training- 12 - 16 March 2018 at **ULJ**, Faculty of Medicine. (**Prof. dr Perunović**)
2nd training - 26 -29 May 2018 at the **UR**, Faculty of Medicine.
(**Prof. dr Perunović, dr Vlahović**)
3rd training **UF**, 13 - 17 September 2018 at the **UF** at the
Department of Health Sciences (**Prof. Šćepanović, Prof. Perunović, dr Vlahović**)



- **WP3 (Development of LLL courses and interventional pain medicine courses)**

- 3.3. Accreditation of LLL courses in PCs**

- 3.4. Delivering of LLL courses of pain medicine in primary health care centres of PCs**

PHC Indjija (Serbia) : March 23rd 2019 -“Character of chronic pain and treatment”

Accredited within the project (12/6 CME pnt) was organised by the University of Belgrade project team.

Over 150 trained professionals took part in this course.



- **WP3 (Development of LLL courses and interventional pain medicine courses)**

3.4. Delivering of LLL courses of pain medicine in primary health care centres of PCs

July 6th, 2019 – **UBL** , Faculty of Medicine

Pain medicine market need - articulating offer, Dr Z.Vlahović



Recommendations about **PAIN MEDICINE (SUB)SPECIALIST** until 2023:

- **Hospitals: 1 specialist in every single hospital**
- **Outpatient care: 1 specialist per 100.000 people**

- **WP5 (Project dissemination)**
 - 5.3. Promotion of HEPMP program Events**

“Character of chronic pain and treatment”

March 23rd 2019, PHC Indjija, leaflet

“Chronic pain must be treated”


Interview Prof. Dr Stevanović, Večernje Novosti, 05 January 2019

International scientific conference „PAIN - TERRIFYING LORD OF LIFE“


October 22, 2018, SANU

IV Congress of intensive medicine,

Novi Sad, 29 – 31.03. 2019.

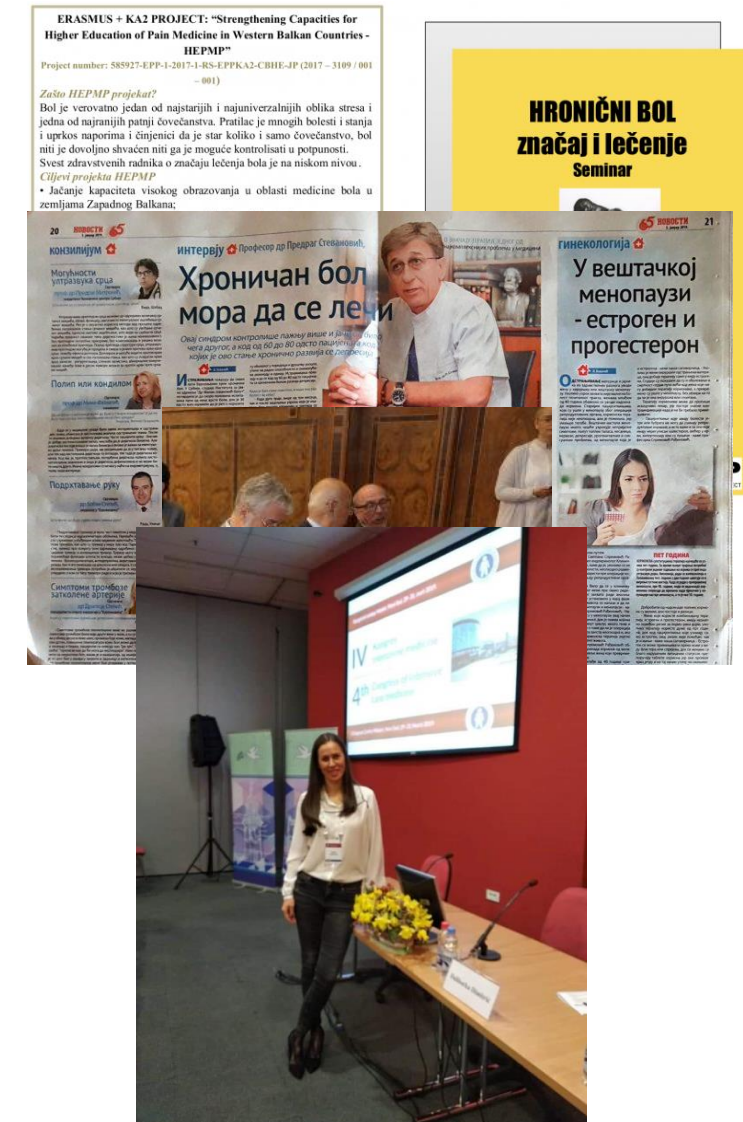

- **WP5 (Project dissemination)**
 - 5.5. Dissemination of institutional websites, newsletter, promotional material and media**



- **WP7 (Management)**

7.3. Kick off meeting

Belgrade on 8-9 December 2017 at the Faculty of Medicine of the University of Belgrade.

7.4. Regular management board meeting

- 1st meeting (at the time of Kick-off meeting)
- 2nd meeting 15-16 March 2018 UL
- 3rd meeting 28 May 2018 UR
- 4th meeting September 2018 UF



• WP7 (Management)



Project Implementation Report COMMENTS AND RECOMMENDATIONS

Ensure th
partners'

It is diffi
informati
Education
However

Project Number:

585927

Project Title:

Strengthening Capacities for Higher Education of Pain
Medicine in Western Balkan Countries HEPMP

Coordinating Institution:

University of Belgrade

application, field monitoring visits and intermediate report) is that the project impact is moderate for two main reasons. Firstly, not a particularly high number of students planned to be enrolled in the new/updated study programs (only 10 students enrolled per Partner Country Higher Education Institution) will not have a quantitative impact on HE in each Country. The qualitative impact may be higher once the first students graduate from the program.

Secondly, the impact may be increased in terms of quality if numbers of graduates correspond with the labour market needs. To this end a close cooperation and involvement of the private sector representatives (in particular pharmaceutical companies) is a key success factor. The consortium enjoys the participation of the Clinical Hospital Center Dr Dragisa Misovic which is involved in project activities; unfortunately, there are not any of the non-academic partners from Bosnia and Herzegovina and Montenegro.

The project also includes five associated partners, all of them being primary health care centers, two located in Serbia, two in Bosnia and Herzegovina, and one in Montenegro. Participation of these associated partners should be enhanced in view to be of real contribution to the impact of the project.

We recommend intensifying the external communication and the involvement of non-academic partners and to explore the real needs of the market; it will help orient the employability opportunities for future graduates.

Future activities

- WP3 at 3.5. Delivering of interventional pain trainings in PCs (accreditation and realisation of two courses: Course of interventional pain procedures (UR) and Service for acute pain (ULJ))
- WP5 at 5.3. Promotion of HEPMP program Events
- WP5 at 5.4. Developing of institutional websites, newsletter, promotional material and media



Future activities

- To establish **Center for pain medicine** – until the end of 2019, first patients in Center after equipment purchase, until the end of March 2020.
- Strategic plan UCH “Dr Dragisa Misovic-Dedinje” 2016-2021. (strategic programs of Clinic of for Anesthesiology)

Center for pain medicine (will be part of the Clinic for for Anesthesiology)

- cancer and non-cancer pain
- 5 beds in day hospital for th support (estimate per year . 1100 pat/dh, 2000 pat/amb)
- multidisciplinary team (neurologist, oncologist, radiologist etc)
- Equipment : EHO, Rtg, X ray C - arc

Financing

- 1st instalment of the first pre-financing - spent
- 2nd instalment of the first prefinancing – paid
- UCH “Dr Dragisa Misovic –Dedinje” participated in costs and financed one amount of travel costs



Thank You and Welcome!
